

Facilities Update

DECEMBER 20TH, 2018





Franklin High School Concessions

<u>Project Status</u>	Completed	Scope	Project includes the construction of a new Concessions Building adjacent to the stadium of the high school. The building will have concession windows facing both the stadium and the adjacent baseball and playing fields.
Contractor	GL Group, Inc.	Summary	Interior punch list items have been completed. The pricing fo the pipe enclosure was approved, and the GC is proceeding.
Total Budget	\$954,250.00	Contract	\$1,144,000.00
Substantial Completion	June 2018	New Contract Amount	\$1,145,125.85









Franklin High School Tennis Courts

Project Status	Completed	Scope	Complete reconstruction of the six (6) existing tennis courts.
Contractor	Halecon	Summary	The project was awarded to Halecon of Bridgewater, NJ. All work has been completed and this is now in project close-out.
Total Budget	\$840,000.00	Contract	\$847,917.00

New Contract Amount \$811,484.25







New Contract Amount

\$355,058.85

MacAfee Road Elementary School Toilet Renovations

Project Status	Completed	Scope	Project includes the renovation of four (4) gang Toilet Rooms—in order to make them ADA compliant (similar to the renovations to the toilet rooms at the Pine Grove Manor School).
Contractor	Nadiad Inc.	Summary	All work in the Toilet Rooms has been completed. The GC is completing any remaining Punch List items.
Total Budget	\$367,000.00	Contract	\$323,000.00










MacAfee Road Elementary School Toilet Renovations

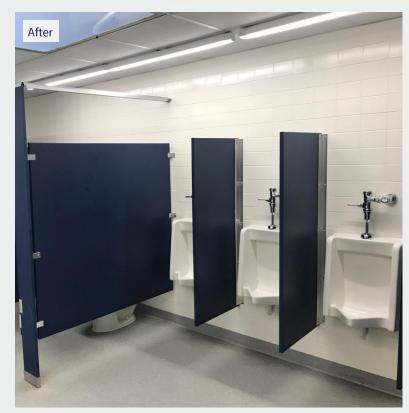








Conerly Road Elementary School Site Improvements

Project Status	Completed	<u>Scope</u>	Project includes repair to a ramp (and railings) at the rear of the school building.	
Contractor	Nadiad Inc.	Summary	All work is complete. The Punch List was forwarded to the GC.	
Total Budget	\$35,000.00	Contract	Contract amount was combined with the MacAfee Toilet Rooms.	



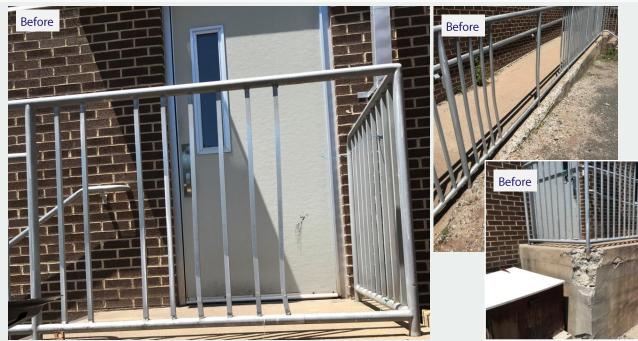






Conerly Road Elementary School Site Improvements



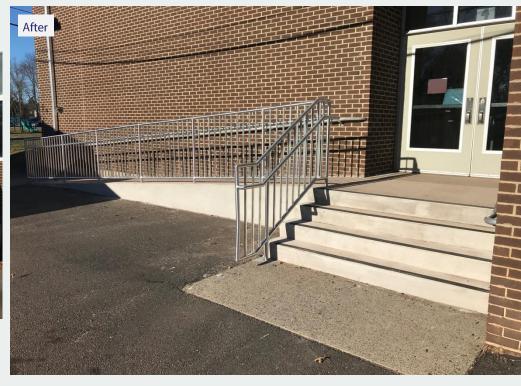







District-wide Windows/Door Replacements

Project Status	Under Construction	<u>Scope</u>	Complete reconstruction of the six (6) existing tennis courts.
Contractor	Panoramic Window and Door Systems, Inc.	Summary	The windows for the Hillcrest School are ready for installation. A meeting was held at the school on October 26th —with the District and School Administrators, the GC, as well as Eric Clarkson from AHERA, the District's environmental engineer—in order to discuss the scheduling of the abatement and the installation of the new windows. Work at Hillcrest is in progress (see picture below). The windows at Conerly will be scheduled next with MacAfee the last school to have the new windows installed.
Total Budget	\$1,700,000.00	Contract	\$1,399,000.00


Hillcrest Elementary School | Budget: \$645,200.00



MacAfee Road Elementary School Budget: \$376,900.00



Conerly Road Elementary School Budget: \$376,900.00





Windows/Doors Replacements





District-wide Windows/Door Replacements

Hillcrest Elementary School









Pine Grove Manor Exterior Door Replacements

<u>Project Status</u>	Completed	Scope	Replace the exterior doors at the Pine Grove Manor School, with an alternate bid to replace several of the interior wood flush doors.
Contractor	Jersey Architectural Door & Supply	Summary	The replacement of the doors is nearly completed. Work has been completed and a Punch List walk-through will be done the first week of January.
Total Budget	\$128,000.00	Contract	\$161,702.00










Pine Grove Manor Exterior Door Replacements

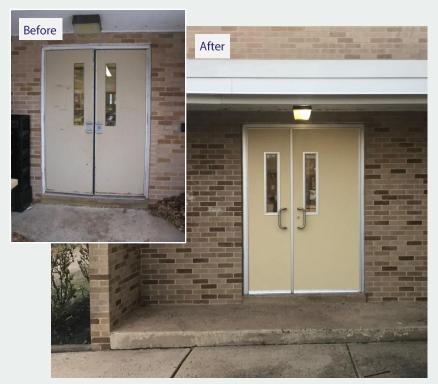






Project Status	Partially Completed	<u>Scope</u>	Project includes the replacement of the existing unit ventilators at Elizabeth Avenue.
			Project includes providing an enlarged Multi-Purpose Room, Cafeteria and Kitchen and reconfiguring the spaces now occupied by the Media Center and the Lobby/Admin spaces.
			Project includes the addition of new Pre-Kindergarten, Kindergarten and upper level Classrooms and all required ancillary spaces.
Contractor	Patock Consruction	Summary	Additions and site work are complete; new kitchen expected be on line January 2019.
Total Budget	\$11,203,144.00	Contract	\$12,024,314.00
Substantial Completion	MP Room: December 2017; Addition: April 2018; Renovation: September 2018	New Contract Amount	\$12,755,098.72






Site Plan

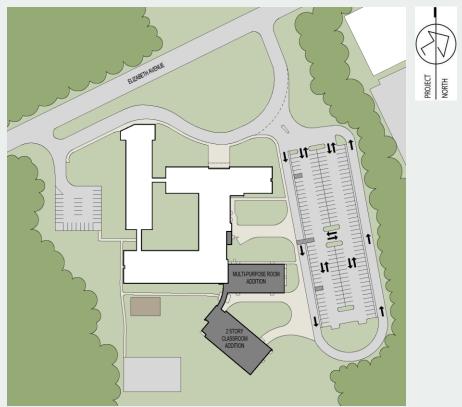





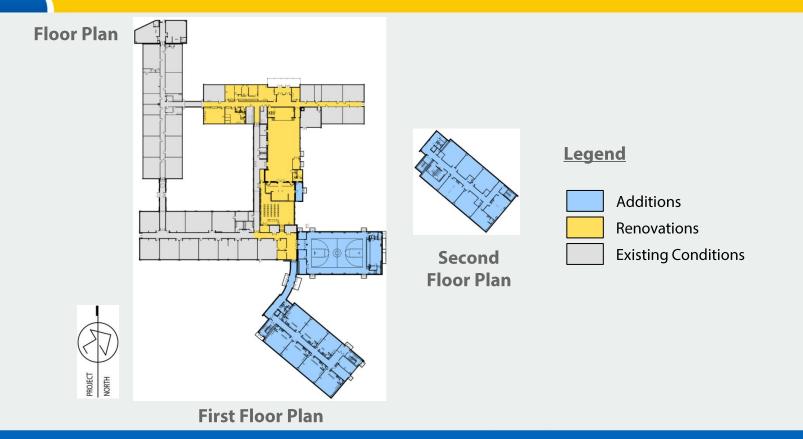






Renovated Hallway



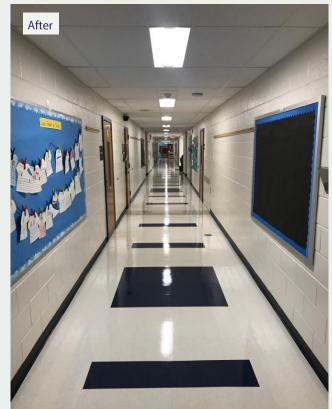





Renovated Lobby









Renovated Main Office







Renovated Classrooms









Renovated Media Center













Rendering







Finished Additions







Rendering













Parking Lot Expansion








Multi-Purpose Room



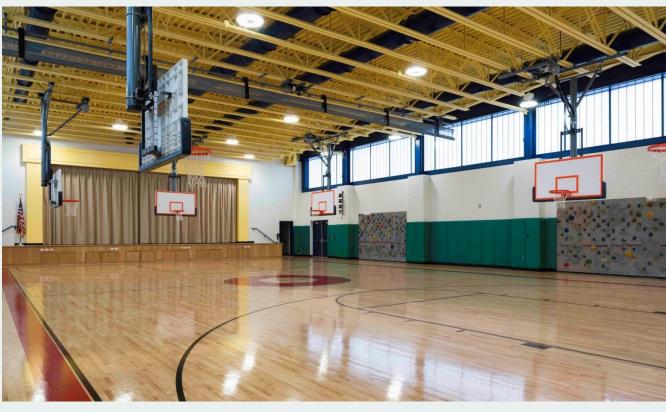





Corridors in New Addition









Classrooms







DRG Architects

200 Franklin Square Drive, Suite 402 Somerset, NJ 08873
